


# Security Infrastructure Projects and Device Purchases Metrics

| SECURITY INFRASTRUCTURE PROJECTS AND DEVICE PURCHASES |                        |                |                   |
|---|------------------------|----------------|-------------------|
| PROJECT BUDGET  | CONSTRUCTION           | ARCH/ ENGINEER | FF&E & TECHNOLOGY |
| Security Infrastructure Projects and Device Purchases | \$ -                   | \$ -           | \$ 11,419,495     |
| <b>SUB TOTAL</b>                                      | \$ -                   | \$ -           | \$ 11,419,495     |
| <b>TOTAL PROJECT BUDGET</b>                           | <b>\$ 11,419,495</b>   |                |                   |
| PROJECT ENCUMBRANCES                                  |                        |                |                   |
| Construction  | \$ -                   | \$ -           | \$ -              |
| Architect Fee   | \$ -                   | \$ -           | \$ -              |
| Engineer Fee  | \$ -                   | \$ -           | \$ -              |
| City Permitting Fee                                   | \$ -                   | \$ -           | \$ -              |
| Furniture Fixtures & Equipment                        | \$ -                   | \$ -           |                   |
| Technology (Entech)                                   | \$ -                   | \$ -           | \$ 1,774,984.60   |
| <b>SUB TOTAL</b>                                      | \$ -                   | \$ -           | \$ 1,774,984.60   |
| <b>TOTAL PROJECT ENCUMBRANCES</b>                     | <b>\$ 1,774,984.60</b> |                |                   |
|   |                        |                |                   |
| <b>TOTAL PROJECT BALANCE</b>                          | <b>\$ 9,644,510</b>    |                |                   |



| 2020                          |     |     |     |     |      |      |     |      |     |     |     | 2021 |     |     |     |     |      |      |     |      |     |     |     | 2022 |     |     |     |     |      |      |     |      |     |     |     |
|-------------------------------|-----|-----|-----|-----|------|------|-----|------|-----|-----|-----|------|-----|-----|-----|-----|------|------|-----|------|-----|-----|-----|------|-----|-----|-----|-----|------|------|-----|------|-----|-----|-----|
| Jan                           | Feb | Mar | Apr | May | June | July | Aug | Sept | Oct | Nov | Dec | Jan  | Feb | Mar | Apr | May | June | July | Aug | Sept | Oct | Nov | Dec | Jan  | Feb | Mar | Apr | May | June | July | Aug | Sept | Oct | Nov | Dec |
| ← Purchase and Installation → |     |     |     |     |      |      |     |      |     |     |     |      |     |     |     |     |      |      |     |      |     |     |     |      |     |     |     |     |      |      |     |      |     |     |     |

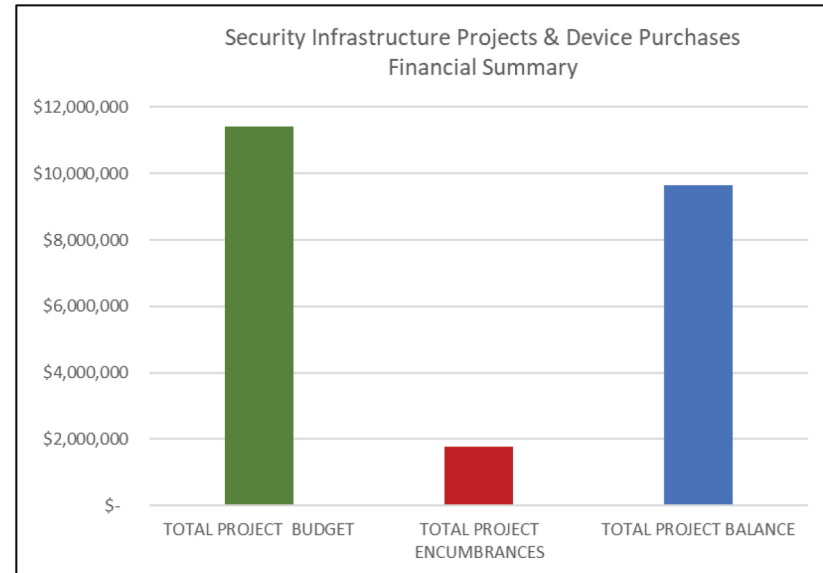
