


# SUMMER 2010 RENOVATION AND CONSTRUCTION PROJECTS REPORT

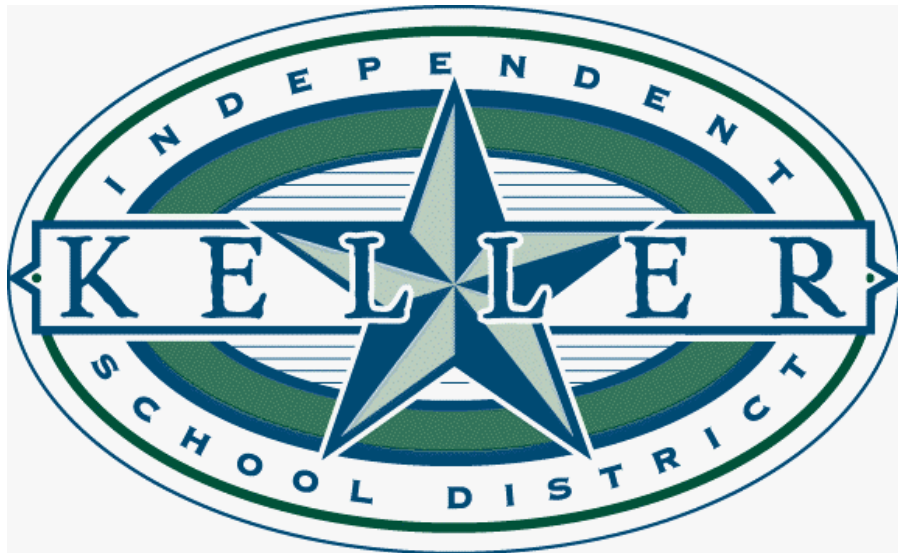

## Summer 2010 Projects

Keller Early Learning Center & Timberview Middle School -

Video of Keller Early Learning Center Building and the  
New Timberview Middle School Campus.

## Summer 2010 Projects

### Renovation & Addition Projects -

#### District Wide athletic improvement projects:

- Keller High School Field house Renovation is on schedule and contractor intends for building to be ready by mid August.
- Transformer has been moved at the Natatorium Building and the foundation for the Addition has started.

#### Fossil Ridge High School Black Box & Scene Shop Addition:

- Renovation work is scheduled to begin the week of June 7<sup>th</sup>.

## Summer 2010 Projects

### Re-roofing Projects & Temperature Controls Projects -

#### Roofing Projects -

- Contractor will be starting at Bear Creek Intermediate School and Whitley Road Elementary after school lets out.
- Roofing projects at the Learning Center and Willis Lane Elementary will start in July.

#### Temperature Controls -

- Contractor has been installing controls at Bear Creek Intermediate, Florence Elementary, Freedom Elementary, & North Riverside Elementary.
- They will be working at Hidden Lakes Elementary, Parkwood Hill Intermediate, Lone Star Elementary, Keller Harvel Elementary, Fossil Hill Middle School, Indian Springs Middle, and Fossil Ridge HS.

## Summer 2010 Projects

### Planning & Bidding of Elementary No. 22 -

#### Project Milestones -

- Construction Drawings are scheduled to be complete and printed by July 12<sup>th</sup>.
- Construction Manager will be advertising and bidding the project July and August and is scheduled to submit a Guaranteed Maximum Price for the Project at the second Board Meeting in August.

## Summer 2010 Projects

### Capital Improvement Projects on Existing Campuses -

#### Interior Renovation Projects -

- Parkview Elementary Life Skills Classroom Renovation
- Hillwood Middle School Main Entry Renovation

#### Concrete Repair Projects -

- Freedom Elementary front loop drive and bus drive is scheduled to be replaced.
- Sidewalk and Drainage repairs are scheduled at Indian Springs Middle School, Independence Elementary, and Bear Creek Intermediate School.

#### Flooring and Painting Projects -

- Florence Elementary, Chisholm Trail Intermediate, and Fossil Ridge High School Field house.

## Summer 2010 Projects

### Facility Modification Requests On Existing Campuses -

- Over 65 small campus renovation or landscape improvement projects were submitted for consideration.

### Ancillary Bus Parking Lot Project -

- Scheduled to receive bids on the project May 28<sup>th</sup>.
- Scheduled to present to the School Board on June 21<sup>st</sup>.

Summer 2010 Projects

# Questions
